
TENANT IMPROVEMENT PLAN & FLOOR LAYOUT

Prepared Specifically for 6400 Sierra Court, Suite E, Dublin, CA 94568 · 96,000 Sq. Ft. Leased


6-MONTH BUILD-OUT
$5,300,000 TI BUDGET (CASH)

Aligned to the 6400 Sierra Court, Suite E Architectural Drawings (Dublin Sierra LLC): Per the existing Suite E plans, the premises feature a **high-bay ground floor (~78,600 SF architectural; 30' clear height, ~40' column grid)** and an **existing unoccupied second-floor mezzanine (~19,400 SF)** along the south frontage (**96,000 SF leased**). Our TI plan keeps the exterior walls, roof, slab, columns, and 2nd-floor structure intact, uses **overhead water supply piping (no water lines installed in or under the concrete slab)**, and modifies the existing automatic sprinkler system per City of Dublin & Alameda County Fire codes.

1. ARCHITECTURAL FLOOR PLAN — GROUND FLOOR & EXISTING 2ND-FLOOR MEZZANINE (96,000 SF LEASED)

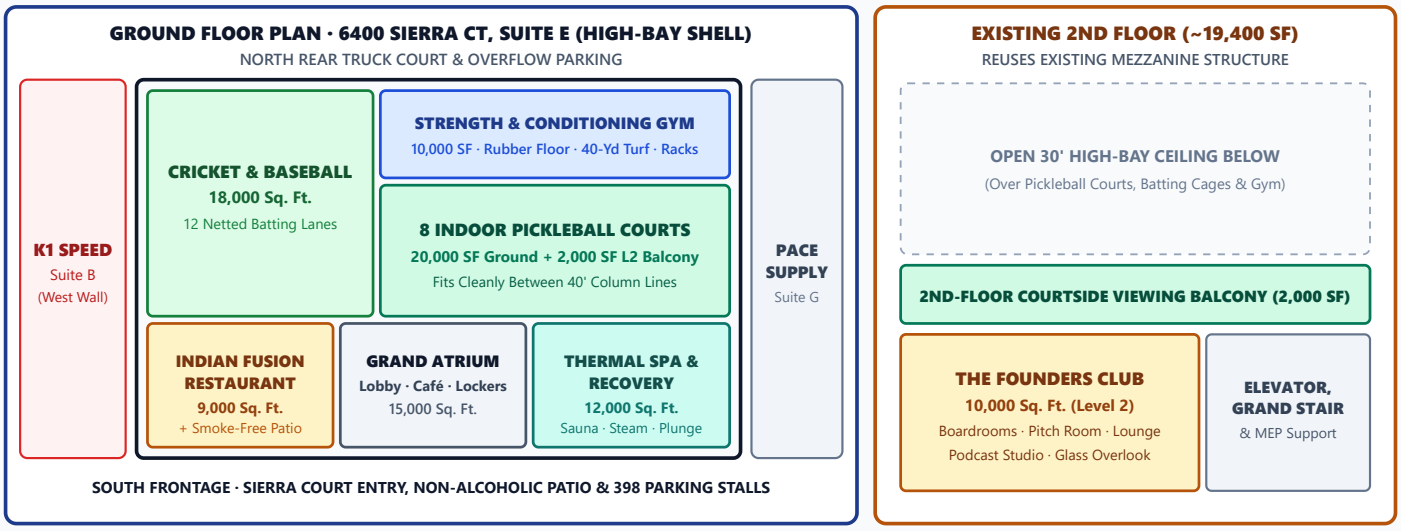

2. 3D FACILITY LAYOUT & ARCHITECTURAL RENDERINGS (6400 SIERRA COURT, SUITE E)

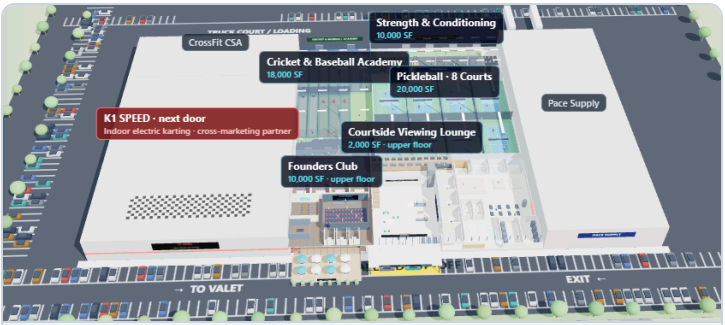

3D Cutaway Model of Suite E: Shows exact fit between K1 Speed (west) and Pace Supply (east), with front valet drop-off and smoke-free patio on Sierra Court.



Interior Finish Standard: Acoustic wall panels, indirect LED sports lighting, warm wood & glass mezzanine railings, and resort-grade locker/spa finishes.

ZONE-BY-ZONE TENANT IMPROVEMENT ESTIMATES


Complete Breakdown of the $5,300,000 Build-Out + $1,200,000 Cash Reserve ($6,500,000 Total)

~$55 / SQ. FT. INTERIOR FIT-OUT
100% CASH FUNDED

1. DETAILED TENANT IMPROVEMENT (TI) COST ESTIMATE BY BUILDING ZONE

BUILDING ZONE & SQUARE FOOTAGE	SPECIFIC CONSTRUCTION & EQUIPMENT SCOPE	ESTIMATED COST
1. Permits, Architecture & Site Prep All 96,000 Sq. Ft.	Architectural/MEP/sprinkler drawings, City of Dublin building/use & Alameda County health permits, ADA path/signage & interior slab prep	**$450,000**
2. HVAC, Electrical & High-Bay Lighting Building-Wide Systems	Glare-free indirect LED sports fixtures, HVAC zoning/dehumidification, electrical sub-panels & fire sprinkler head adjustments per code	**$850,000**
3. 8 Indoor Pickleball Courts & Balcony 22,000 Sq. Ft. (Ground + L2)	Multi-layer cushioned acrylic tournament court surfacing over existing slab, padded column wraps, acoustic panels, curtains & L2 viewing glass	**$550,000**
4. 12 Cricket & Baseball Batting Lanes 18,000 Sq. Ft. (Ground NW)	12 full-length retractable ceiling-hung netting tunnels, high-density turf, programmable bowling/pitching machines, video kiosks & bleachers	**$600,000**
5. Indian Fusion Restaurant & Patio 9,000 Sq. Ft. (Ground SW)	Commercial kitchen, Type-1 exhaust hoods, grease trap, clay tandoor ovens, overhead water supply piping, 110-seat dining room & patio	**$950,000**
6. Thermal Spa, Saunas, Plunge & Lockers 12,000 Sq. Ft. (Ground SE)	Above-slab waterproofed wet-zone build, overhead water supply lines, 2 cedar saunas, 2 steam rooms, cold plunges, 4 treatment rooms & lockers	**$850,000**
7. Strength & Conditioning Gym 10,000 Sq. Ft. (Ground NE)	Heavy-duty rubber athletic flooring, 40-yard sled sprint turf lane, Olympic lifting racks, dumbbells, functional rig & commercial cardio row	**$450,000**
8. Upstairs Founders Club, Lobby & Café 10,000 SF L2 + 15,000 SF Atrium	Finish existing unoccupied 2nd floor into executive lounge, 4 meeting rooms, boardroom, pitch theater & podcast studio; ground lobby & café	**$600,000**
TOTAL TENANT IMPROVEMENT & EQUIPMENT	**Complete Turnkey Build-Out of 6400 Sierra Ct, Suite E (~$55 / Sq. Ft.)**	**$5,300,000**
9. Pre-Opening Rent, Deposit & Cash Cushion	Covers 6 months build-period rent ($888,000), security deposit ($150,000) & opening cash cushion ($162,000)	**$1,200,000**
TOTAL CASH COMMITTED BY TENANT	**100% Cash Funded by Precision Developers (No Bank Loan Contingency)**	**$6,500,000**

2. VISUALS OF KEY INTERIOR BUILD-OUT ZONES



Ground-Floor Sports Zones (40,000 SF Combined): Pickleball courts, batting cages, and strength gym install directly over the existing concrete slab with zero structural cutting.



Concentrated Wet Zones (21,000 SF Combined): Spa, locker rooms, and kitchen are grouped along the South frontage with overhead water piping per Suite E building standards.

6-MONTH BUILD SCHEDULE & OPENING CASH FLOW

Month-by-Month Timeline from Lease Signing (Month 1) to Positive Cash Flow (Month 9)

6 MONTHS TO OPEN DOORS
MONTH 9 POSITIVE CASH FLOW

1. MONTH-BY-MONTH CONSTRUCTION & OPENING SCHEDULE (MONTHS 1 TO 12)

MONTH	PHASE	KEY ACTIVITIES AT 6400 SIERRA COURT, SUITE E	MONTHLY RENT PAID	MONTHLY NET CASH FLOW
Month 1	**Permits & Plans**	Lease signed; $6.5M cash committed; submit TI & sprinkler drawings to City of Dublin; order hoods, saunas & court surfacing.	$148,000 (From Reserve)	Build Phase (Pre-Funded)
Month 2	**Permit Approval**	City permit & use sign-off; contractor mobilizes; interior slab prep, layout marking & 2nd-floor partition framing begin.	$148,000 (From Reserve)	Build Phase (Pre-Funded)
Month 3	**Rough-In Work**	Overhead water supply & electrical rough-in for kitchen & spa; high-bay LED lighting & HVAC ducting installed in main bay.	$148,000 (From Reserve)	Build Phase (Pre-Funded)
Month 4	**Courts & Cages**	Pickleball cushion courts laid; 12 cricket/baseball netting tunnels hung; saunas, steam rooms, hoods & L2 glass installed.	$148,000 (From Reserve)	Build Phase (Pre-Funded)
Month 5	**Equipment & Fit**	Gym racks/turf, bowling/pitching machines, tandoor/appliances, cold plunges, lounge furniture & AV installed.	$148,000 (From Reserve)	Build Phase (Pre-Funded)
Month 6	**Inspections & Open**	Final City Building, Fire & Health inspections; Certificate of Occupancy issued; staff training & Grand Opening.	$148,000 (From Reserve)	**DOORS OPEN**
Month 7	**Month 1 Open**	Grand Opening month ($350,000 revenue vs. $430,000 operating cost incl. rent; -$80k covered by Cash Reserve).	**$148,000**	($80,000) (From Reserve)
Month 8	**Month 2 Open**	Memberships, youth academies & restaurant covers ramp to $450,000/mo revenue vs. $450,000/mo total costs.	**$148,000**	**$0 (Break-Even)**
Month 9	**Month 3 Open — POSITIVE CASH FLOW**	**Monthly revenue reaches $500,000/mo vs. $460,000/mo total operating costs (including $148,000/mo rent).**	**$148,000**	**+$40,000 / mo**
Months 10–12	**Months 4–6 Open**	Monthly revenue grows from $560,000/mo to $640,000/mo; first 6 months open produce **+$350,000 positive net cash flow**.	**$148,000 / mo**	**+$90k–$170k/mo**
Year 2 & Year 3+	**Full Operation**	**Year 2: $7,500,000 revenue (+$2,000,000 net cash flow). Year 3+: $8,880,000 revenue (+$3,180,000/yr net cash flow).**	**$152k–$157k/mo**	**+$265,000 / mo**

Summary for the Sellers & Listing Broker:

- **How Much to Build: $5,300,000** interior build-out & equipment + **$1,200,000** cash reserve = **$6,500,000 Total Cash Committed (No Bank Loan)**.
- **How Long to Build: 6 Months** from lease signing to opening doors (using the existing shell & second floor with no structural demolition).
- **When Positive Cash Flow Starts: Month 9 from lease signing (Month 3 after opening doors)**, growing to **+$2,000,000/yr in Year 2** and **+$3,180,000/yr in Year 3+**.
